



Pellicano Drive Widening Project


*Commissioners Court Regular Session
Planning & Development Department
Transportation, Planning & Engineering Division
August 1, 2022*

Project Description

- **Project Team:**
 - Project Management: Camino Real Regional Mobility Authority
 - Design Consultant: CEA Group
 - Construction Management: Atkins
 - Construction Contractor: JAR Concrete
 - Contract Amount: \$ 21,655,645.80
- **Scope:**
 - Limits from Joe Battle Boulevard (Loop 375) to Darrington Road
 - Six-lane Divided Roadway
 - Bike Lanes | Hike & Bike Trails
 - Illumination, Landscaping & Stormwater Management
- **Current Delays**
 - COVID-19
 - Crew & Materials Availability
 - Unforeseen Utility Conflicts (Older Area of Development)
- **Possible Future Delays**
 - Cement Availability
 - Utilities Unforeseen Conditions
 - Materials Availability

Proposed Project Phase Timeline

For Planning Purposes – Subject to Change

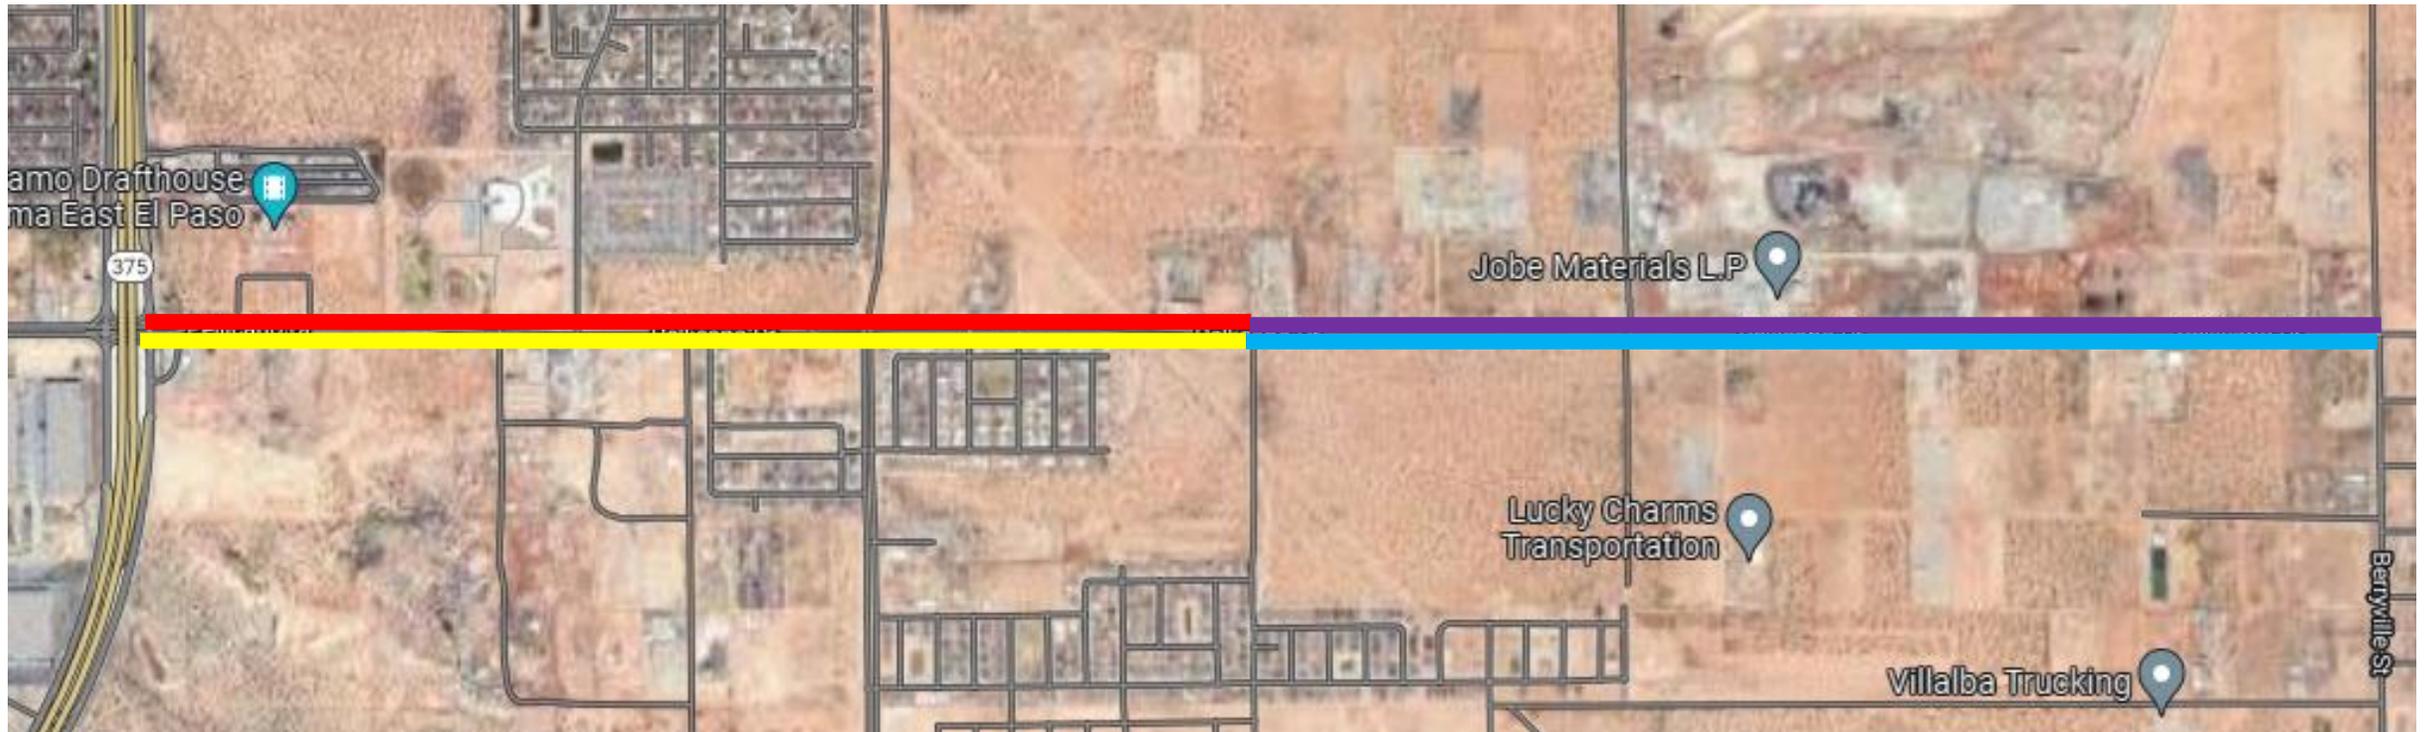

-  Westbound Loop 375 to Aircoupe (September 2022)
-  Westbound Aircoupe to Darrington (September 2022)
-  Eastbound Aircoupe to Darrington (January 2023)
-  Eastbound Loop 375 to Aircoupe (Complete)

Community Notice & Outreach

- Completed Presentations to Partner Agencies
 - County Commissioners Court (6-6-22)
 - Camino Real Regional Mobility Authority (CRRMA) Board (6-8-22)
 - Transportation Policy Board (MPO) (6-17-22)
 - Horizon City Council (7-12-22)
- Future Presentations to Partner Agencies
 - El Paso City Council (8-2-22)
 - Transportation Project Advisory Committee (TPAC) MPO (8-3-22)
 - Socorro Independent School District (TBD)

July Completed Activities

- Joe Battle Blvd. to Sun Fire Blvd.
 - Flexible Base installation completed to 75%
 - Prime Coat installed from TxDOT driveway to Sun Fire Blvd.
 - Relocation of Fire Hydrants completed
 - Median demolition completed, arranging for concrete pavement
- Sun Fire Blvd. to Aircoupe Way
 - Setting rebar for concrete pavement at 25%
- Aircoupe Way to Darrington Rd.
 - Installed Flexible Base where water loops were installed
 - Setting rebar for concrete pavement at 50%

Flexible Base prime coated from Sun Fire Blvd. TxDOT driveway



Finalizing Flexible Base installation from Joe Battle Blvd. to TxDOT driveway



Median demolition by Joe Battle completed



Rebar installation from Aircoupe to Darrington



August Forecasted Activities

- Joe Battle Blvd. to Sun Fire Blvd.
 - Finalize installation of Flexible Base
 - Installation of Hot Mix
 - Installation of Rebar
- Sun Fire Blvd. to Aircoupe Way
 - Finalize rebar installation
- Aircoupe Way to Darrington Rd.
 - Finalize rebar installation (Jobe to Darrington)
 - Installation of Concrete Pavement (Jobe to Darrington)
 - Install Hot Mix where the Water Loops were installed
 - Finalize Embankment and Start Installation of Flexible Base (Aircoupe to Jobe)
 - Installation of Rock Wall
 - Start excavation of Pond C and storm sewer connection to Pond



Questions?

